

LA PERLA

06-Mar-26

BNW PROJECT STATUS




Project Information		Construction Progress	
Project Name	La Perla	Soil Investigation	100%, Completed
Project Description	2B+G+6+R	Topography Survey	100%, Completed
Plot No	MRA 64	Pre CPT	100%, Completed
Location	Al Marjan Island RAK	Soil Improvement	100%, Completed
Plot Boundary - Fence and Branding Banner	100%, Completed	Post CPT	100%, Completed
RERA Approved Project Finish/Handover Date	31-Dec-27	Shoring	Mobilization - 100%, Completed Shoring Works - 100%, Completed PTP Piles , Inprogress

SITE PROGRESS PHOTOS



PTP Pile Reinforcemet and Placement Inprogress

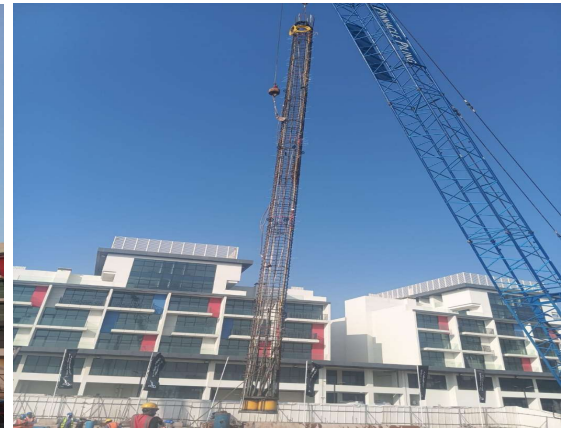

PTP Pile reinforcement Inprogress



PTP Piling Works Inprogress



PTP Piling Works Inprogress
