

AQUA MAYA

06-Mar-26

BNW PROJECT STATUS



Project Information		Construction Progress	
Project Name	Aqua Maya	Soil Investigation	100%, Completed
Project Description	2B+G+9	Topography Survey	100%, Completed
Plot No	MRA 52	Pre CPT	100%, Completed
Location	Al Marjan Island RAK	Soil Improvement	100%, Completed
Plot Boundary - Fence and Branding Banner	100%, Completed	Post CPT	100%, Completed
RERA Approved Project Finish/Handover Date	31-Dec-27	Shoring	Mobilization 100%, Completed Shoring Works 99%, In Progress PTP Piles, Inprogress


SITE PROGRESS PHOTOS



Pre Excavation Site Preparation



Excavation and PTP works Preparation Inprogress

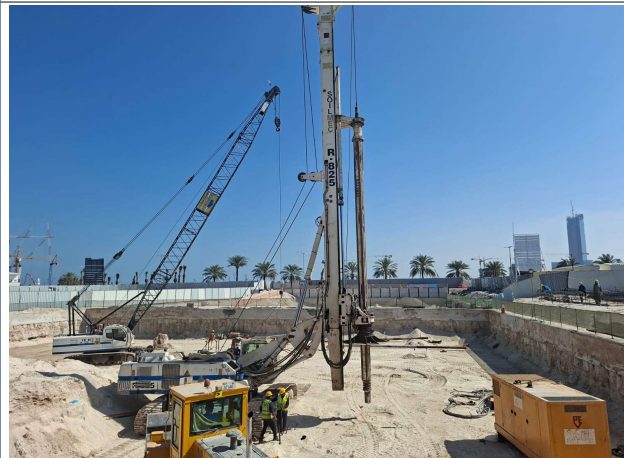

Excavation ad PTP works Preparation Inprogress



PTP Piles Reinforcement Inprogress
